

## PIERCE SCHOOL WEEKLY UPDATE



**SPECIAL NOTE:** Full Building Demolition has begun, and a larger piece of equipment will arrive on 12/18 to support the demolition. Anticipate more activity on the School Street side of the site, including concrete hammering and trucks entering and exiting the site.

### **THIS WEEK** (December 9-13)

- Brick/conc removal, abatement and trucking.
- Obtain demo permit, begin demolition of 1974 building, adjacent to Library on School Street.

### **PROJECT TRACKING:**

- Brick abatement 90% complete
- Building Demolition 4% complete

### **ANTICIPATING NEXT WEEK** (December 16-20)

- Complete exterior abatement
- Large excavator arrives on site for demo
- Continue with building demolition

### **MILESTONES:**

- Demo begins, 1974 Bldg. (B): 12/11/24
- Support Of Excavation (SOE) begins: 01/06/25


For other project details, please visit the Project Website: <https://www.brookline.k12.ma.us/Page/2463>

To sign up for Project Updates, please go to: <https://www.brooklinema.gov/list.aspx?ListID=816>



# PIERCE SCHOOL BUILDING PROJECT

## Demolition Progress as of 12/13/24

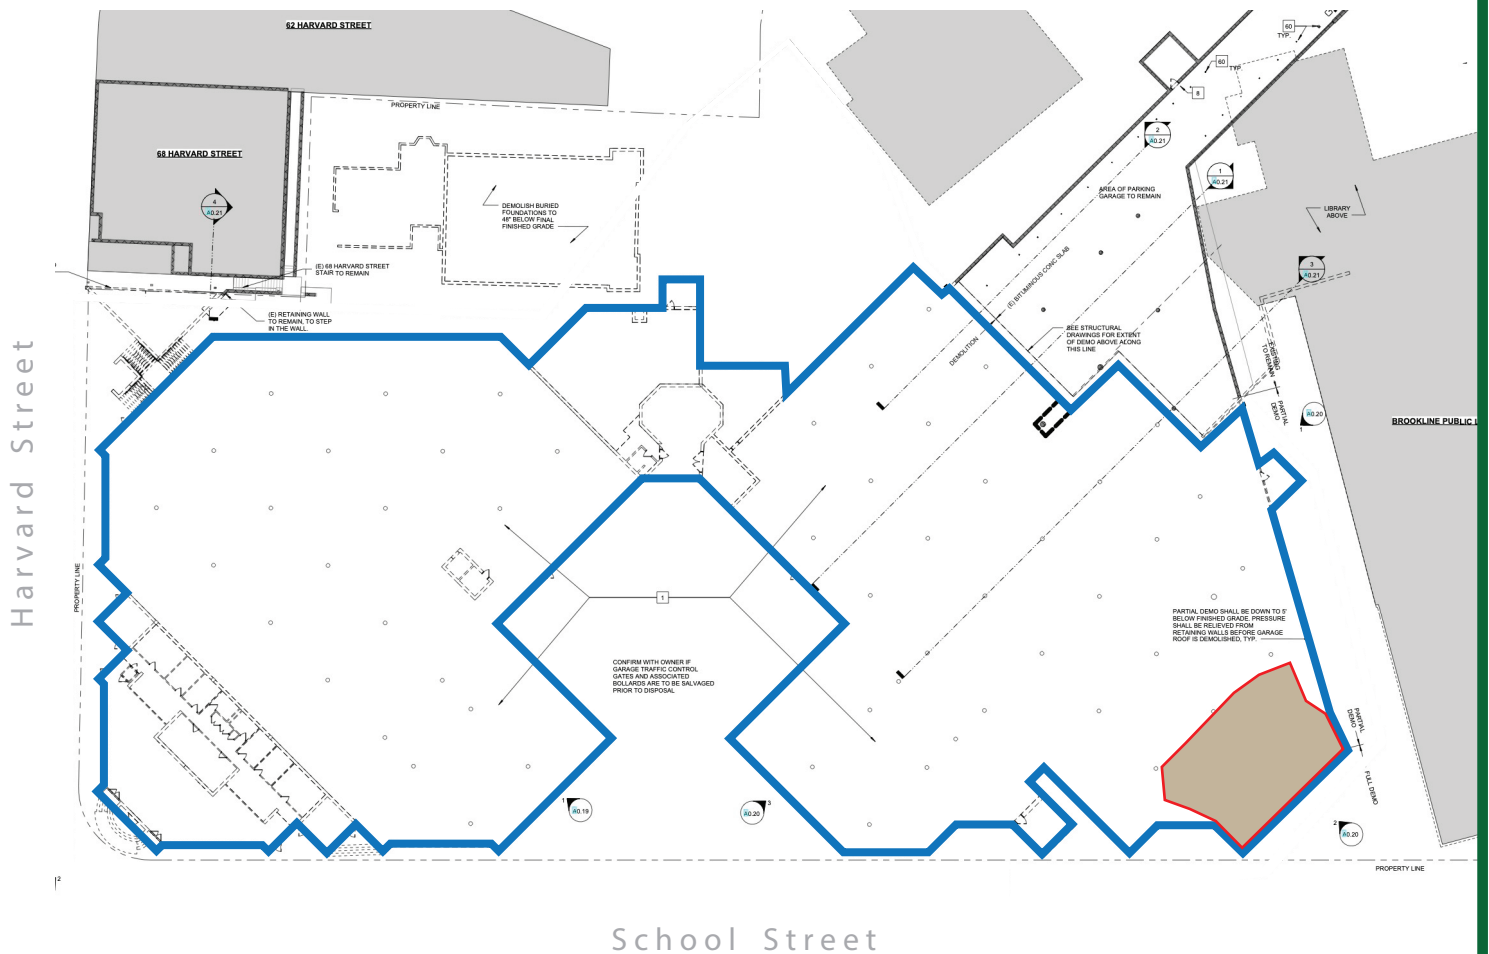

Current demolition

Completed demolition
