

PIERCE SCHOOL WEEKLY UPDATE



NOTE: Demolition is paused while the demo debris is processed, sorted and trucked out.

THIS WEEK (January 13-17)

- Processed and sorted concrete/metal debris
- Trucked out materials
- Began preparation for Support of Excavation (SOE) work

PROJECT TRACKING:

- Building Demolition 80% complete

ANTICIPATING NEXT WEEK (January 20-24)

- Process, sort and truck out material
- Begin drilling piles for SOE

MILESTONES:

- Support Of Excavation (SOE) begins: 01/20/25
- Above grade demo complete: 01/31/25

For other project details, please visit the Project Website: <https://www.brookline.k12.ma.us/Page/2463>

To sign up for Project Updates, please go to: <https://www.brooklinema.gov/list.aspx?ListID=816>




PIERCE SCHOOL BUILDING PROJECT

Demolition Progress as of 01/17/25

Please note:

There will be a pause in demolishing the remaining building while the demolition debris is processed, sorted, and trucked out to make room for the remaining work.

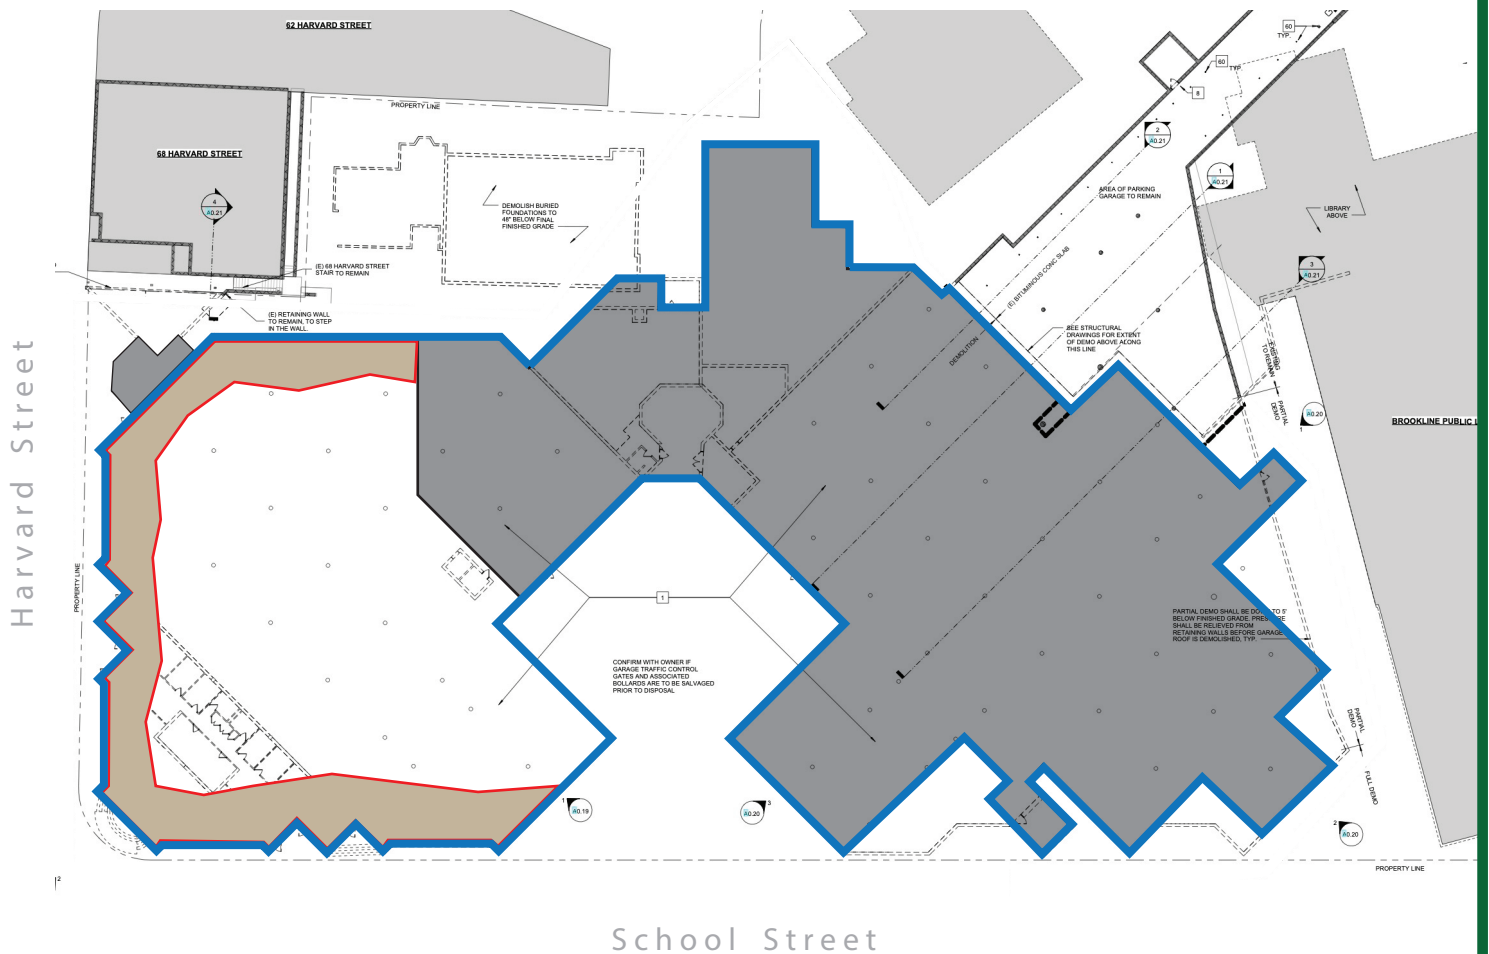

- Demolition this week
- Completed demolition
