

PIERCE SCHOOL WEEKLY UPDATE



NOTE: There will not be a weekly report on 1/10/25.

THIS WEEK (Dec. 30-January 3)

- Demolition continued
- Trucked out scrap metal and demo debris
- Post-abatement air quality check at Library and Day Care

PROJECT TRACKING:

- Building Demolition 60% complete

ANTICIPATING NEXT WEEK (January 6-10)

- Continue with building demolition, towards Harvard Street.
- Truck out stockpiled material

MILESTONES:

- Support Of Excavation (SOE) begins: 01/20/25
- Above grade demo complete: 01/15/25


For other project details, please visit the Project Website: <https://www.brookline.k12.ma.us/Page/2463>

To sign up for Project Updates, please go to: <https://www.brooklinema.gov/list.aspx?ListID=816>



PIERCE SCHOOL BUILDING PROJECT

Demolition Progress
as of 01/03/25

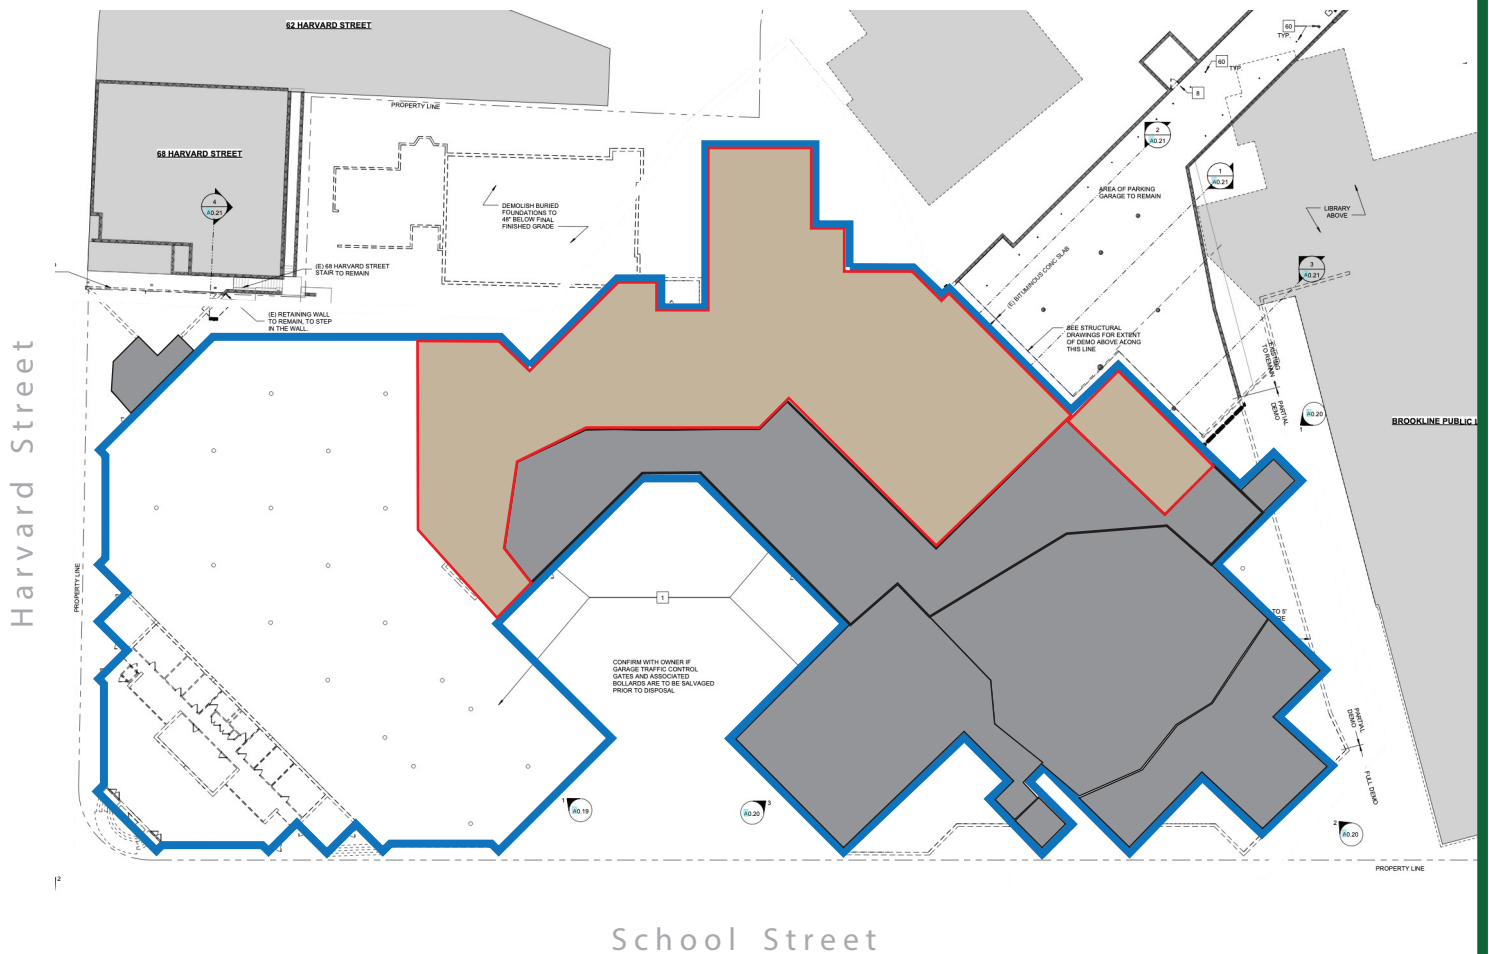

- Demolition this week
- Completed demolition
